



Central University of
Technology, Free State

WORK INTEGRATED LEARNING IN INFORMATION TECHNOLOGY

Central University of Technology, IT Department

Group K

Gumede N	221046289
Khiba SP	223073835
Khunyeli P	224125791
Makara K	221009228
Mchaisa M	223037875
Motlhakane M	223095490
Modisana MD	224004511
Phahlane LG	223078534
Ramotete KJ	222055729
Semela K	224054263

Group Mentor:
Date of Submission:

Table of Contents

1. Introduction.....	4
Purpose of Document.....	4
Stakeholder Profile.....	4
Project Scope.....	4
2. Current Business Process.....	5
Current Business Process Description.....	5
Current Business Process Diagram.....	6
3. Problem Statement.....	7
4. Overall Description.....	8
Purpose Perspective.....	8
User Classes.....	8
Operating Environment.....	9
Project Deliverables.....	9
Project Constraints.....	9
Assumptions.....	10
Exclusions.....	10
5. Requirements.....	11
6. Project Feasibility.....	13
Technical Feasibility.....	13
Operational Feasibility.....	14
Economic Feasibility.....	15
Schedule Feasibility.....	15
Legal Feasibility.....	16
Ethical Feasibility.....	17
Feasibility Summary.....	17
Overall Feasibility Decision.....	18
7. Risk Register.....	19
8. Requirements Change Log.....	20
9. Appendix A.....	21
10. Appendix B.....	22
11. Appendix C.....	26

12. Appendix D.....	27
13. Appendix E.....	28
14. References(GitHub & Superbase links).....	28
15. Approvers and Sign-Off.....	29

Revision History

Date:	Version:	Description:	Author:
24/08/26	01	Original	Motlakane
28/08/26	02	Edited	Motlhakane
30/08/26	03	Edited	Modisana
30/08/26	04	Edited/Final	Phahlane

1.Introduction

1.1 Purpose of Document

This Software Requirements Specification serves to outline the functional and non-functional requirements of the Event Décor Management and Self-Service Estimation system. The document will be used by the development team as well as the relevant stakeholder who will be involved in verifying whether the functionality of the proposed solution is deemed correct and approved for production.

1.2 Stakeholder Profile

AkeaEvents is currently operated by the primary stakeholder, Ms. Keneilwe, who resides in Johannesburg, alongside her co-owners, her two sisters. The stakeholder is responsible for the overall management of the business as initial connection is made through her and coordination of the business such as client communication, understanding décor requirements, quotation preparation, conducting services, sourcing materials requested and overseeing the delivery of décor services booked.

The co-owners provide operational and administrative support required, from reviewing quotations, setting up décor furniture to outsourcing materials required that are not available. Collectively, Ms. Keneilwe and her sisters manage most of the business activities internally, with current control over client communication, service delivery and ensuring décor projects are executed.

Where additional assistance or manpower is compulsory for larger events, temporary workers are outsourced.

1.3 Project Scope

The aim of this solution is to simplify the business process that AkeaEvents uses to provide event décor services to its users by enabling customer self-service as well as improving overall decision-making and productivity of the business owner as she performs her business operations. The solution also aims to eliminate any client uncertainties or doubts thus increasing direct agreements between the client and business owner more quickly.

The system must provide the necessary functionality for users to browse previous décor work catalogues, create enquiries or booking requests and generate estimated quotations.

The system must also provide business owners with the ability to efficiently handle and manage client enquiries or requests, view client reports and summaries and post additional previously done décor work.

Key objectives include:

- Reducing the volume of unnecessary back-and-forth communication during the initial quotation process with client.

- Transferring mundane responsibilities of the business owner over to the solution to increase efficiency and productivity.
- Improving Persistence of previous event details, customer contact info and Quotation estimates for future use.
- Providing a reliable and consistently available platform for clients and business users.

2. Current Business Process

This section aims to describe and illustrate the main daily business workings that AkeaEvents implement to make their business function. The following information has been extracted via an interview with the stakeholder which was conducted on the 24/08/2026.

[A detailed summary of the interview questions and answers from the stakeholder interview is presented in Appendix B]

2.1 Current Business Process Description

2.1.1 Customer Discovery

Customers mainly discover the business through completed work posted on TikTok, Instagram and Facebook.

2.1.2 Initial Contact

Interested customers contact the business through WhatsApp. At present, these communications are handled through the business owner's personal WhatsApp number.

2.1.3 Needs Assessment

The business asks customers questions to determine what services and equipment are required. These may include chairs, tables, tents or a complete décor service, as well as the customers' event date and venue.

2.1.4 Quotation Creation

The business would create an itemized quotation through an application that was downloaded from Google Play Store. Inside the quotation would reveal a list of all the items and equipment as well as their prices that would be included for the event as per the customers' request and an additional service fee.

2.1.5 Internal Review

Before a quotation is sent to the customer, the business partners review it and verify its accuracy. One internally approved it is sent to the customer.

2.1.6 Customer Approval

Customers may request changes to the quotation, such as adding, removing or adjusting individual items. The quotation is then updated accordingly. After the quotation has been approved, **50% of the total fee** is to be paid upfront. This will allow the official full commencement of the requested décor service.

2.1.7 Décor Setup

The equipment will be delivered to the specified venue, and the décor will be stylized according to the client's request **1-2 days** before the actual event. The final payment will be made **one week** before it begins. The equipment will then be returned the day after the event.

2.2 Current Business Process Diagram

[A mid-level visual representation of the Business Process is presented in Appendix A]

2.3 Problem Analysis

The stakeholder identified several challenges in the current process.

2.3.1 Vague or Incomplete Customer Requests

Customers are not always specific about their requirements when they initially contact the business. This results in additional questions and repeated communication before an appropriate quotation can be prepared.

2.3.2 Volatile Flower Pricing

Fresh flower prices fluctuate according to the season. Because customers may not be able to wait several days for updated flower prices, the business sometimes estimates these costs in advance. This creates a risk of undercharging if the actual market price is higher.

2.3.3 Manual and Time-Consuming Quotation Process

The most significant problem identified by the stakeholder is the manual quotation process. Every quotation is individually prepared, and customers currently have no way to obtain a rough estimate themselves.

The stakeholder explained that this problem creates significant back-and-forth communication, particularly when customers make last-minute requests. It also contributes to pricing risks and places pressure on the business to respond quickly.

2.3.4 Unrealistic Customer Timelines

Customers sometimes underestimate the time required to prepare quotations and organize event requirements. This can result in last-minute requests that place additional pressure on the business.

3. Problem Statement

The event décor business currently relies on manual customer communication and individually prepared quotations. Customers primarily contact the business through the owner's personal WhatsApp number and must communicate their requirements before receiving a quotation.

This process is time-consuming because quotations must be prepared individually, reviewed and revised when customers change their requirements. Customers may also provide incomplete information or submit requests at short notice. As a result, the business would experience increased administrative workload, customer back-and-forth and pricing-related pressure.

This would in turn leave customers feeling unsatisfied as the inaccurate prices in the quotations would reveal what they feel to be unrealistic and could potentially prompt them to back out of the overall service that was requested which normally results in reduced profits for the business due to the fall out.

Therefore, the business requires an integrated digital platform that can reduce manual quotation work, improve customer self-service, centralize customer requests and provide the business with better visibility of its quotation and conversion process.

4. Overall Description (Project Scope)

4.1 Product Perspective

The project will focus on developing an integrated event décor management solution that enables customers to explore décor services, generate self-service quotation estimates and create event requests or bookings whilst also providing the business users with a centralized system for managing customer inquiries, quotations, bookings, portfolio content and customer conversion information.

4.2 User Classes

User Classes	Role in the system
Admin (Mobile app User) (Stakeholder)	Their role is to manage customer inquiries, quotations, bookings, portfolio content and customer conversion information.
Client (WebApp User)	Their main responsibilities include generating self-service estimates, exploring a showcase portfolio of previous events handled by AkeaEvents and creating enquiries.

4.3 Operating Environment

- The **mobile application** must be able to operate on **Android** mobile devices.
- The **website** must operate correctly on Androids and Desktops.
- The website must be available on the latest version of the following web browsers: **Microsoft Edge, Google Chrome, Firefox**
- **RAM** recommendation for both devices is **128MB** optimal experience.
- **Strong internet** is recommended for better experience.

4.4 Project Deliverables

- **Flutter mobile and desktop application** – used by the business to manage customer requests, portfolio information and bookings.
- **ASP.NET web application** – used by customers to browse décor work, view services, generate estimates and submit inquiries
- **Supabase backend** – used to store and manage the information shared between the customer and business applications.
- **Working prototype** – demonstrating the main customer and business functions.
- **GitHub repository** – containing the project code, documentation and evidence of group work.
- **Project management documents** – including the Microsoft Project schedule and ITC327W Project Progress Tracker.

4.5 Project Constraints

4.5.1 Time Constraints

The project needs to be completed within the allocated WIL timeframe. This gives the team limited time to gather requirements, develop the system, test it, complete the documentation, and submit the final project. Because of the limited time available, the project scope needs to remain manageable so that the team can complete the required work before the deadline.

4.5.2 Technology Constraints

The project must use the required Flutter, ASP.NET and Supabase technologies

4.5.3 Stakeholder Availability

The overall success of the project depends on the stakeholder and business partners being available to provide feedback and confirm requirements.

4.5.4 Resource Constraint

The system is being developed by a student group, so development time, technical skills and other resources are limited. The most important features will therefore be developed first.

4.5.5 Implementation and Design Constraint

All relevant data must be pulled from one centralized database. The entire solution will only cater towards users who can speak the English language.

4.6 Assumptions

- Both mobile and web applications must run 24/7
- Customers will have internet access when using the applications.
- The business will remain responsible for confirming final bookings and arrangements
- The estimator must provide an accurately estimated price.
- The users of the solution must be capable of speaking English.

4.7 Exclusions

The following areas will not be included in the main version of the system:

- Managing the physical storage of décor equipment.
- Managing physical transport and delivery.
- Managing the people involved in setting up events.
- Controlling physical décor equipment.
- Advanced AI recommendations for décor.

- Processing customer payments.

5. Requirements

ID	Requirement	Type	Priority	Related Stakeholder need
FR1	System must provide customers with an accurate cost estimator.	Functional	Must Have	Customers can generate an instant estimate based on their requirements.
FR2	System must provide a showcase portfolio of AkeaEvents previous works	Functional	Must Have	Customers can browse previous work before contacting the business.
FR3	The mobile and desktop application must provide business users with the relevant data to manage customer requests	Functional	Must Have	The business can manage incoming customer requests and enquiries.
FR4	The owner can upload new portfolio items (images, descriptions, pricing)	Functional	Must Have	Keep the portfolio current with new work
NFR1	Both Applications must have close to 100% uptime	Non-Functional	Could Have	The applications must be operating 24/7
NFR2	The web application must be compatible with Google Chrome, Edge and Firefox	Non-Functional	Must Have	Business users should be able to view the website across multiple web browsers.

NFR3	The mobile application must be compatible for Android users	Non-Functional	Must Have	Customers should be able to download the application on their mobile devices.
NFR4	Business Related information should only be accessible to the admin	Non-Functional	Must Have	The stakeholders can have access to all customer requests, enquiries and bookings from the Web.
NFR5	The system must handle large volumes of data without risking performance	Non-Functional	Could Have	The applications must be able to handle an abundance of Customer requests
IR1	Both applications must share the same data using one centralized database on Superbase.	Integration	Must Have	The business should be able to manage customer requests, quotation requests and bookings.
SR1	All portfolio, pricing, and inquiry data stored centrally in Superbase for both apps	System	Must Have	N/A
SR2	Flutter mobile app + ASP.NET web app, both backed by one shared Superbase instance	System	Must Have	N/A
SR3	Two user roles: public/customer (view + self-service) and owner/admin (full access)	System	Must Have	Owner wants the two access levels reflected: customer vs owner

6. Project Feasibility

This feasibility study assesses whether the proposed solution built using the Asp .Net + Flutter + Supabase technologies for AkeaEvents is realistic to design, build, and deliver within the academic semester, given the group's current skills, the stakeholder's availability, and the project's scope. It draws on the stakeholder interview, the SRS, the project schedule, and the group's own self-assessed skills. Its findings feed directly onto the Project Risk Register: each feasibility concern raised below corresponds to one or more identified risks.

6.1 Technical Feasibility

Question	Group Finding
Does the group have the required Flutter skills?	Not yet at a confident level; Flutter skills are still developing across the group and will need to be built up during the project.
Does the group have the required ASP.NET skills?	Basic familiarity only. Only a few members have been introduced to the built-in components (ASP.NET Core Identity, MVC) that ASP.NET has to offer.
Can the group work with Supabase?	Limited prior experience; Supabase is new to most of the group and will require self-teaching.
Are suitable development computers available?	Yes — group members have personal laptops suitable for Flutter and ASP.NET development.
Are suitable test devices available?	Yes — group members have installed smartphone emulators on their PC for testing the Flutter app, and the relevant browsers for testing the ASP.NET app.
Is reliable internet access available?	Mostly yes, though not always guaranteed for every member.

Technical Feasibility Decision: Feasible with changes

The group has access to the required tools, and the core functions (portfolio, estimator, booking form) are achievable. However, Flutter, ASP.NET, and Supabase integration skills are still developing, so more advanced functions should be simplified or postponed.

6.2 Operational Feasibility

Question	Group Finding
Will the prototype address the stakeholder's problem?	Yes — it replaces the manual, WhatsApp-only quoting process with self-service browsing, estimating, and booking.
Who will use the mobile application?	The business owner and her two business partners.
Who will use the web application?	Prospective and existing customers.
Do the intended users have suitable devices?	Yes. Customers have suitable devices, as they already use smartphones to communicate with the business through WhatsApp and to access social-media and advertising platforms such as Facebook and TikTok. This indicates that they have access to devices capable of supporting the proposed application..
Do users have suitable internet access?	Customers are reached via social media, implying general internet access; the owner's constraint is her limited available time, not connectivity.
Will the proposed solution fit the organization's current activities?	Yes — it digitizes the existing process (browse portfolio → get estimate → book → delivery) rather than replacing it.
Will users require guidance or training?	Customers should not need training, given a simple self-service flow; the owner and partners may need a short walkthrough of the admin dashboard.
Are any proposed functions unsuitable for the intended users?	No — the proposed functions were chosen to mirror the owner's existing manual steps in digital form.

Operational Feasibility Decision: Feasible with changes

The proposed solution fits AkeaEvents' current operations well, but the stakeholder's very limited feedback availability (evenings only, unavailable Thursdays) means the group must agree fixed, recurring meeting times to make development and validation practical.

6.3 Economic Feasibility

Resource	Available?	Action Required
Internet access or data	Available (mostly)	Confirm backup options for members without reliable data.
Transport to the stakeholder	Not Needed	Stakeholder prefers meetings to be held virtually (Microsoft Teams)
Development computers	Available (personal laptops)	None.
Test devices	Available	None.
Required software	Available	Ensure all members install and configure the necessary tool versions.
Supabase resources	Available (free/hobby tier)	Monitor usage to stay within free-tier storage and API limits.
Presentation resources	Available (existing office/slide tools)	None.

Economic Feasibility Decision: Feasible

There are no cost barriers to completing the prototype; all required tools and resources are available to the group at no direct cost.

6.4 Schedule Feasibility

Question	Group Finding
Is there enough time available for the system design?	Yes, provided the group finalizes scope early using this feasibility and risk process.
Is there enough time available for Flutter development?	Most likely, Dependant on the group's skill level
Is there enough time available for ASP.NET development?	Yes, most members are competent in using this framework.
Is there enough time available for Supabase integration?	Tight; early testing is needed to avoid discovering integration issues late in the schedule.
Is there enough time available for testing and corrections?	Only for integration and beta testing.
Is there enough time available for stakeholder feedback?	Constrained by the stakeholder's evening-only, no-Thursday availability;

Are too many functions currently included?	Yes
Which functions may need to be simplified, postponed or removed?	Full funnel analytics, WhatsApp/chatbot integration, multi-tier role-based permissions, and production uptime infrastructure.

Schedule Feasibility Decision: Feasible with changes

The project is achievable within the semester only if scope is reduced to the core functions and stakeholder feedback times are locked in early to avoid delays.

6.5 Legal Feasibility

Question	Group Finding
Will the prototype collect personal information?	Yes — customer name, contact details, and event details submitted through the booking form.
Is all the information necessary?	Yes; only the information needed to process an inquiry or booking is collected.
Who should be allowed to access the information?	Only the business owner and her two business partners, via authenticated admin accounts.
Will test data be used during development?	Yes; the group will use test/sample data rather than real customer data during development and testing.
How will passwords and private keys be protected?	Managed through Supabase Auth and environment variables/secrets, never committed to source code or GitHub.
Does the project involve confidential stakeholder information?	Yes; pricing structures and portfolio content are business sensitive.
Is private stakeholder information being kept out of GitHub?	Yes; the group will use .gitignore and avoid exposing real pricing, credentials, or customer data in the public repository.

Legal Feasibility Decision: Feasible

No legal barrier prevents the project, provided the group follows basic data-handling discipline throughout development, consistent with the requirements of South Africa's POPIA.

6.6 Ethical Feasibility

Question	Group Finding
Does the stakeholder understand the purpose of the project?	Yes, confirmed through the structured stakeholder interview and the proposed SRS sent to her for review.
Is unnecessary personal information being collected?	No; only the information needed to process an inquiry or booking is collected.
Could the proposed solution negatively affect intended users?	No significant risk identified, provided cost estimates are clearly marked as indicative, not final quotes.
Is information being used only for its intended purpose?	Yes; customer data collected is used only to respond to that customer's inquiry.
Does the proposed prototype accurately reflect stakeholder needs?	Yes, based on the structured interview conducted directly with the stakeholder.
Are users being treated fairly and responsibly?	Yes; no group of users is disadvantaged or excluded by the proposed design.

Ethical Feasibility Decision: Feasible

No ethical concerns were identified, provided cost estimates are clearly labelled as indicative and customer data collected during the project is treated as test data.

6.7 Feasibility Summary

Feasibility	Decision	Main Reason	Change Requires
Technical	Feasible with changes	Core Functions achievable, but Flutter/ASP.NET/Superbase skills still developing	Learn and test integration early: simply advanced functions

Operational	Feasible with changes	Fits the existing process well, but stakeholder feedback windows are narrow	Agree a fixed, recurring evening feedback slot
Economic	Feasible	All required tools and resources are available at no cost	Monitor Supabase free-tier usage
Schedule	Feasible with changes	Core scope is achievable in the semester; the full feature list is not	Postpone or simplify lower-priority functions
Legal	Feasible	No legal barrier; POPIA-relevant data can be handled carefully	Keep credentials and private data out of GitHub
Ethical	Feasible	No ethical concerns identified	Clearly label estimates as indicative

6.8 Overall Feasibility Decision

Decision: The project is feasible with changes

The proposed project is feasible with changes. The main strengths of the project are that the group has free access to all required development tools (**Flutter, ASP.NET, and Supabase**), the core stakeholder-requested functions (**portfolio browsing, a self-service cost estimator, and a booking form**) are technically straightforward to build with these tools, and there is no budget barrier since all chosen technology is free for student use. The main limitations identified are that the group's hands-on experience with Flutter, ASP.NET, and Supabase integration is still developing, and the stakeholder is only reliably available for feedback after 6pm on weekdays and is unavailable on Thursdays, which narrows the windows available for requirements confirmation and review. To ensure that the project can be completed within the semester, the group will prioritize the essential functions (**portfolio, booking form, and a simple admin view**), postpone lower-priority or higher-effort functions (**WhatsApp/chatbot integration**) to a later phase, and agree a fixed recurring feedback time with the stakeholder early in the project.

These findings and conditions form the direct basis for the risks recorded in the Project Risk Register.

7. Risk Register

ID	Risk Statement	Category	L	I	Score	Level	Mitigation	Contingency	Owner	Status
R1	Stakeholder is only reliably available after 6pm on weekdays, not Thursdays, which may delay feedback	Stakeholder	3	2	6	Medium	Agree a fixed recurring evening feedback slot early	Request written feedback; use previously confirmed requirements	Motlhakane M	Open
R2	Stakeholder may take longer than expected to respond outside her limited availability window	Stakeholder	2	2	4	Medium	Send requests with a clear response deadline attached	Escalate via an alternate contact (business partner) if urgent	Modisana MD	Open
R3	Group's current Flutter/ASP.NET/Supabase skills are still developing, which may slow development	Technical	3	3	9	High	Assign learning tasks; test basic integration early	Simplify affected function; reallocate task	The group	Open
R4	Group may struggle to connect Flutter, ASP.NET, and Supabase correctly (shared auth/database)	Technical	2	3	6	Medium	Build and test a small integration example before full development	Simplify the affected function	The group	Open
R5	Development tasks may take longer than the schedule allows, leaving little time for testing	Schedule	2	3	6	Medium	Build in buffer time; prioritize core functions first	Cut lower-priority functions to protect testing time	Khiba SP	Open
R6	Limited overlap between group and stakeholder availability may cause scheduling conflicts	Schedule	3	2	6	Medium	Fix recurring meeting times in advance	Request async/written feedback when live meetings aren't possible	Semela K	Open
R7	Uneven participation among group members could leave tasks incomplete	Team	2	3	6	Medium	Allocate clear tasks; monitor contributions weekly	Reassign urgent tasks; record the concern	Makara K	Open
R8	Poor or infrequent communication between group members could cause duplicated work or missed deadlines	Team	2	2	4	Medium	Use a shared group chat and a weekly check-in	Escalate persistent issues to the course facilitator	Ramotete KJ	Open
R9	Limited access to reliable internet, laptops, or devices could delay development or testing	Resources	1	2	2	Low	Identify backup devices/locations early	Temporarily reassign affected tasks to another member	Phahlane LG	Open
R10	Customer/business data could be exposed if Supabase access rules are set up incorrectly	Data & Security	2	3	6	Medium	Test and review access rules before go-live	Restrict access immediately; audit and correct rules	Gumede N	Open
R11	Limited testing time before submission could mean bugs remain in the estimator or booking flow	Quality	2	2	4	Medium	Reserve dedicated testing days in the schedule	Prioritise fixing high-impact bugs before submission	Khunyeli P.	Open
R12	The client-facing web application may not be user-friendly for mobile users	Technical	3	2	6	Medium	Perform testing on both Mobile and desktop devices	Simplify affected function.	Mchaisa M	Open

8. Requirements Change Log

#	Original Requirement	Change	Reason
1	Initial scope included direct WhatsApp/chatbot API integration for customer notifications.	Descoped to an in-platform inquiry form only.	Reduced integration complexity to fit the semester timeline; identified during feasibility review.
2	Initial scope included a full analytics/reporting dashboard.	Reduced to basic counts (inquiries, estimates, conversions) for the prototype.	Full analytics identified as a Phase 2/stretch feature; not achievable within available time.
3	Initial discussion considered multi-tier role permissions.	Simplified to a single shared owner/admin role for the prototype.	Reduces authentication complexity; stakeholder confirmed all three partners perform the same tasks.

9. Appendix

Appendix A

Stakeholder interview questions

Q1. Can you explain how your current process works; from the time a customer contacts you until the décor service is completed?

Q2. Who participates in this process, such as the business owner, employees, customers, or other people?

Q3. What problems or challenges do you currently experience when managing customer requests, bookings, and events?

Q4. Which of these problems causes you the greatest difficulty, and why?

Q5. If a mobile application or web system were introduced to help solve this problem, who would be most likely to use the mobile application, the customers or the business owner?

Q6. Who would need to use the web application or management side of the system?

Q7. What important information do you currently need to record and keep track of for each customer or event?

Q8. What would you want customers to be able to do through a mobile application to make the process easier?

Q9. What would you want the business owner or staff to be able to manage through a web application?

Q10. What reports, summaries, or information would help you better manage the business and its activities?

Q11. Who should be allowed to view, update, or manage different types of information in the system?

Appendix B

Interview Q&A summary

This section reveals every question along with a detailed summary of each subsequent answer from the stakeholder:

Q1. Can you explain how your current process works; from the time a customer contacts you until the décor service is completed?

- **Discovery (social media):** Completed work is posted on TikTok, Instagram, and Facebook — this is how most customers first discover the business.

- **Initial Contact (WhatsApp):** Interested customers reach out via WhatsApp, currently all through the business owner's personal WhatsApp number.
- **Needs Assessment:** The owner asks qualifying questions to scope the job — what is needed (chairs only, tables only, tent, or a full décor service) and the event date.
- **Quotation Creation:** An itemized quotation is built using an app downloaded from the App Store, listing every item individually (chairs, tables, under plates, cutlery, crockery, drapes, flowers, décor service fee, transport, etc.), scaled to guest count.
- **Internal Review:** The business partners (sisters) review the quotation for accuracy before it goes to the client.
- **Send to Client:** Once approved internally, the quotation is sent to the customer. ● **Revisions:** Clients often come back wanting to add, remove, or adjust line items, and the quotation is updated accordingly.
- **Booking & Delivery:** (To be confirmed — deposit/payment terms, setup crew, day-of delivery, and breakdown/collection after the event.)

Q2. Who participates in this process, such as the business owner, employees, customers, or other people?

- **The Business Owner and Two Sisters:** The three of them run the business together with no fixed, separate roles — everyone pitches in across communication, quotations, coordination, and setup as needed.
- **Regular Hired Manpower:** For physical setup work (e.g. tents), a regular group of trusted people is called on rather than sourcing casually each time. They are paid for their support, and numbers vary with event scale.
- **The Client:** Central throughout the process — design concepts are shared with them, they give the go-ahead before work proceeds, and they drive the revision stage on the quotation.

Q3. What problems or challenges do you currently experience when managing customer requests, bookings, and events?

- **Vague or Incomplete Customer Requests:** Significant back-and-forth is needed because customers aren't always specific upfront about what they want.
 - **Unrealistic Timelines:** Customers often underestimate how long quoting and preparation takes, leading to last-minute requests.
 - **Limited Storage Space:** Current equipment storage space isn't sufficient for the volume of stock needed.
-

- **Volatile Flower Pricing:** Fresh flower prices fluctuate by season. Since customers can't wait 2-3 days for a quote while the flower market is checked, costs are sometimes estimated upfront — leading to undercharging when actual prices are higher.
- **Manual, Time-Consuming Quoting Process:** Every quote is built individually and manually; customers must reach out and wait for a custom estimate with no way to self-serve a rough price.
- **Proposed Solution — Self-Service Website Estimator:** A website where customers can view past work by event type and generate their own instant, customizable estimate (e.g. selecting event type and guest count) to reduce manual back-and-forth.

Q4. Which of these problems causes you the greatest difficulty, and why?

- The greatest difficulty is the manual, time-consuming quoting process, especially last-minute sourcing, because it touches nearly every other problem at once.
- **Physical and logistical strain:** Short-notice requests mean personally calling around (e.g. checking flower prices) rather than working from a fixed price list.
- **Time-consuming:** Every quote is built manually and individually, so there is no way to give a quick answer.
- **It compounds other issues:** Being manual is also where pricing risk sits (e.g. flower cost fluctuation) and where the most back-and-forth with customers happens, since they are waiting on a person rather than an instant number.
- A website estimator would let customers select what they need and get an instant estimate themselves, removing the bulk of manual back-and-forth. Customers would only make contact once ready to confirm, at which point the business would receive a booking/inquiry notification to follow up on — saving time and reducing pressure to produce accurate estimates on short notice.

Q5. If a mobile application or web system were introduced to help solve this problem, who would be most likely to use the mobile application, the customers or the business owner?

- Both the business and the customers would use the system — it is two-sided.
 - **Business side:** Completed work would need to be consistently uploaded as soon as a job finishes, so the gallery stays current. Queries coming through the platform (WhatsApp, chatbot, or email) would need to be actively monitored and answered.
 - **Customer side:** Customers would browse past work, see pricing, generate their own estimate, and contact the business directly once ready to move forward.
-

Q6. Who would need to use the web application or management side of the system?

- The business owner would manage the system, including uploading completed work/photos, reviewing and responding to customer inquiries and quote requests, and managing bookings/confirmations as customers move from estimate to confirmed order.

Q7. What important information do you currently need to record and keep track of for each customer or event?

- The main focus is tracking the customer journey through the quoting funnel:
- **Inquiries/Leads:** How many people request a quote in a given period.
- **Conversions:** Of those who receive a quotation, how many go on to book/confirm and become paying clients.
- **Drop-offs:** How many people request a quotation but never respond or return, to understand where potential business is being lost.
- Currently there is no structured way to track this — the system should capture it automatically.

Q8. What would you want customers to be able to do through a mobile application to make the process easier?

- Browse past work without needing to ask for a quote first, including full details behind each look (e.g. tent type, guest capacity it was designed for, décor tier, accessories used) alongside the price it cost.
- Select a style/service they like and get an instant estimate without needing to message the business first.
- Self-qualify and decide before making contact — seeing whether something fits their budget and deciding whether to proceed, rather than the business spending time on a lengthy conversation only for the customer to disappear after receiving a quote.

Q9. What would you want the business owner or staff to be able to manage through a web application?

- **Manage and respond to customer requests:** Access and handle incoming inquiries, quote requests, and communication through the platform in one place.
-

- **Fast response times:** Attend to any customer question or request within 24 hours as a maximum turnaround, ideally sooner.
- **System uptime/reliability:** The platform needs to be consistently available, since downtime risks losing potential customers.

Q10. What reports, summaries, or information would help you better manage the business and its activities?


- **Site traffic:** How many people are visiting the site.
- **Self-service estimates created:** How many visitors are generating their own quotation on the platform.
- **Estimate completion rate:** How many people get through to seeing a final estimated cost.
- **Conversion rate:** Of those who see a cost estimate, how many become actual paying customers.
- **Drop-off/abandonment tracking:** How many people start the process but stop partway through, to identify where the process needs improving.
- **Popularity/interest breakdown:** What customers are looking at and gravitating toward most (e.g. kids' parties vs. weddings), to understand what is driving the most business.

Q11. Who should be allowed to view, update, or manage different types of information in the system?

- **Customers:** Can view general/public content (portfolio, pricing estimates, service options) and use the self-service estimation tool, without edit/update permissions.
- **Business Owners (the owner and two sisters):** The only ones who can view, update, edit, or manage business data within the system (bookings, quotations, uploaded work, customer records, reports)

Appendix C

Evidence of stakeholder engagement

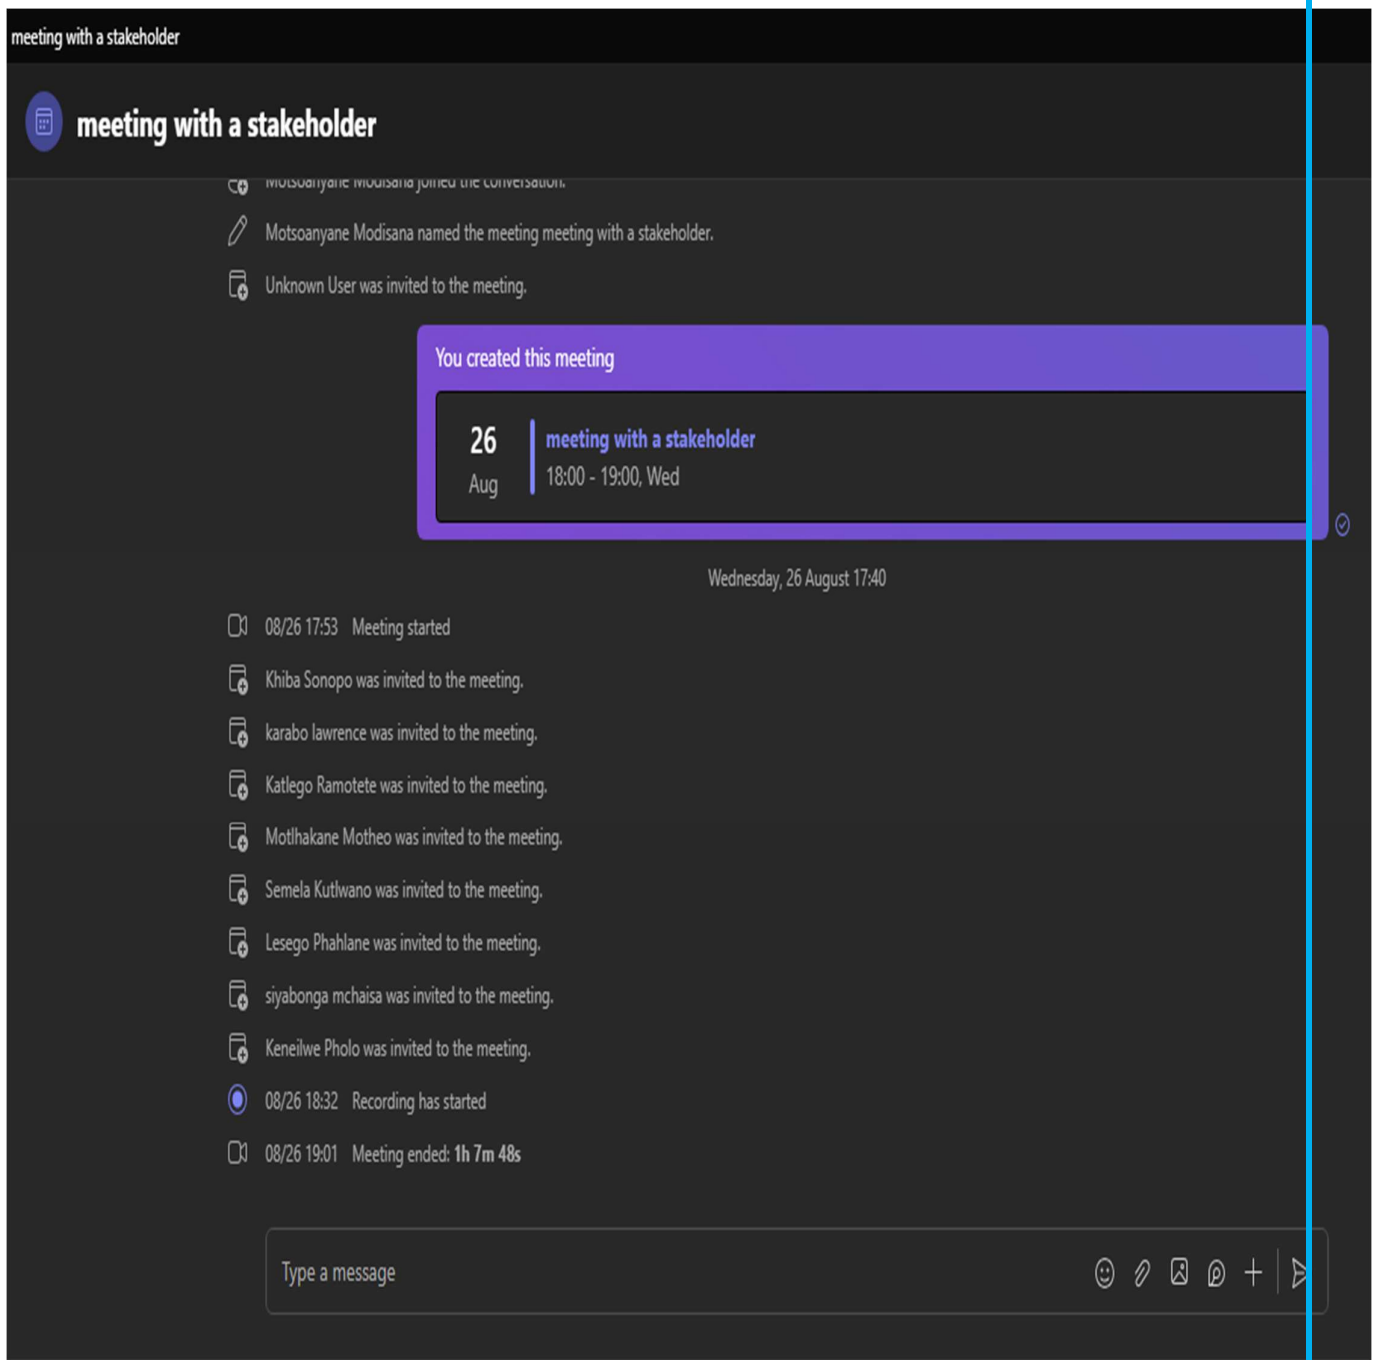

Appendix D

Stakeholder confirmation of the findings through signing



Keneilwe Pholo


to me ▾

Hello Motsoanyane

Please find attached the signed document


On Thu, Sep 3, 2026 at 9:34 PM Motsoanyane Modisana <motsoanyanemodisana8@gmail.com> wrote:

One attachment • Scanned by Gmail ⓘ  Add to Drive



Appendix E

Current Business Process Diagram

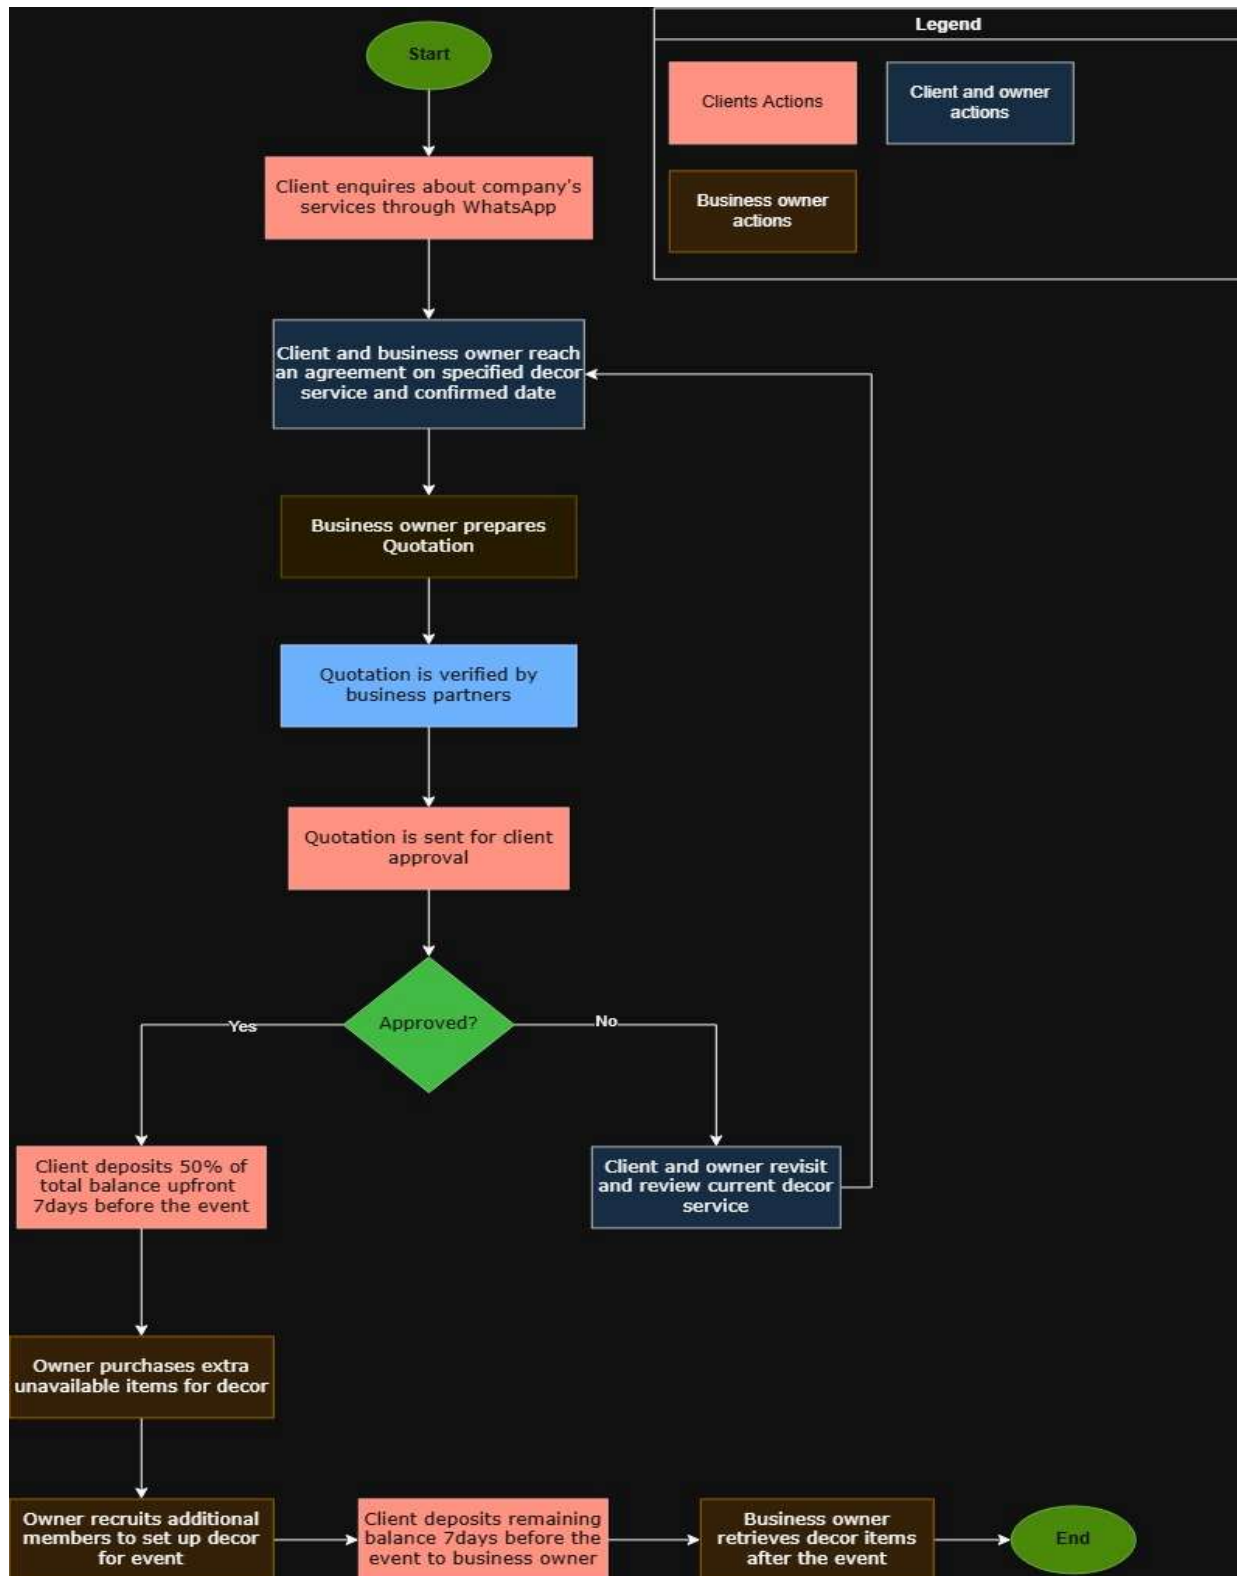

Appendix F

Superbase screenshot

ITC327W FREE / ITC327W Projects / main PRODUCTION Connect Feedback

ITC327W Projects

<https://rsqagixdvwdgmdtnaiod.supabase.co> Copy

STATUS
Healthy

COMPUTE
NANO

GITHUB
Michael-23-bloem/ITC327W

RECENT BRANCH
No branches

LAST MIGRATION
No migrations

LAST BACKUP
No backups

Primary Database
West Europe (London)
eu-west-2 · t3a.nano
CPU 3% · Disk 13% · RAM 46%

Get connected

10. REFERENCES

GitHub link: <https://github.com/Michael-23-bloem/ITC327W.git>

Superbase: <https://rsqagixdvwdgmdtnaiod.supabase.co>

11. Approvers and Sign-off

This section serves to prove that all the outlined requirements have been approved and accepted by the stakeholder and development team.

Name:	Role:	Approved? (Y/N)	Date:
M. Keneilwe	Stakeholder	Yes	03 Sept 2026



Signature of stakeholder
